



Business Central Foundation + Integration Enablement



Gearing your company through an
innovative strategy.



Call us directly?

(44) 7404 240 893

Need support?

info@solutionscallout.co.uk

Business Central Foundation + Integration Enablement

A structured, outcome-led engagement to establish a clean Business Central foundation, connect your operational platform, and leave you with a governed, supportable setup your team can own.

**Governed setup**

Security roles, environments, change control, and “do it once, do it right” configuration patterns.

**Integration-first**

Define the integration contract (data, ownership, cadence, error handling) before building connectors.

**Partner mindset**

Not just “configure BC” — we shape decisions, reduce back-and-forth, and build internal capability.

Commercial options (target: under £15k)


Pick the closest fit now; we lock scope through discovery outputs and a signed “Integration Contract”.

Option	Best for	Durati ion	Fee (Guidan ce)	Notes
Option 1 — Foundation Essentials BC Finance baseline + governance + PoC integration	First-time BC setup, finance-only scope, quick validation	6–8 weeks	£9,500–£12,500	Includes discovery + setup + one integration stream (readiness + PoC).
Option 2 — Foundation + Delivery (Recommended) Essentials + implementation sprints + controlled go-live	Need momentum + a safe go-live path within a 3-month commitment	12 weeks	£12,500 – £14,950	Adds delivery cadence, broader integration hardening, and hypercare.

Fees exclude Microsoft licensing and third-party connector costs. Travel (if any) is at cost with pre-approval.

3-Month roadmap (visual)

This is the “minimum back-and-forth” path: discovery outputs first, then build, then stabilise.

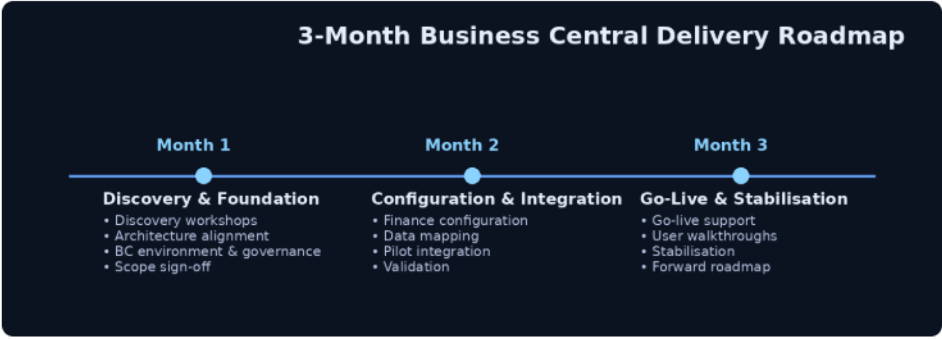

Workplan (tasks, timings, deliverables)

Phase	Weeks	Key tasks	Outputs (definition of done)
1) Discovery & Design Lock	W1–W2	Current-state + target-state mapping BC tenant / environment approach (Dev/Test/Prod) Finance baseline requirements (VAT/MTD, COA, posting groups) Integration Contract: data ownership, payloads, frequency, error handling	Signed scope baseline + backlog (MoSCoW) Integration Contract v1 Security & governance blueprint
2) Foundation Build	W3–W6	BC setup: COA, dimensions, posting, VAT/MTD Master data approach: customers/vendors/items Roles/permissions, approval patterns, audit trail Initial integration build (PoC → working)	Configured BC Finance foundation Integration PoC validated with sample data Runbook + handover notes
3) Stabilise, Train, Go-Live	W7–W12	Integration hardening (monitoring, retries, reconciliation) UAT support + defect triage Cutover planning + opening balances Training + admin enablement + hypercare	Go-live readiness checklist signed Reconciliation pack (source → BC) 30-day stabilisation plan

Engagement model

- Weekly steering check-in (30–45 mins)
- 2x delivery touchpoints per week (build, unblock, validate)
- Shared backlog + decision log (time, rationale, owner)
- Transparent risks + mitigation (no surprises)

What you get at the end

- A clean BC Finance foundation configured to best practice
- An integration contract + working connector path
- Governance runbook (security, changes, support)
- Training + internal capability uplift
